

# MOLTO

## WP1: Management

Olga Caprotti  
University of Gothenburg

# WP1: General view

## In brief

- Leader: UGOT
- Participants: all
- Start: M1, 1 March 2010
- End: M36, 28 February 2013
- Person months: 20pm
- Objectives:
  - Keep the project on track
  - Ensure communication with EU and among partners
  - Coordination of work and financial management

# WP1: General view

## Consortium

1 (coordinator)	Goteborgs universitet	UGOT	Sweden
2	Helsingin yliopisto	UHEL	Finland
3	Universitat Politècnica de Catalunya	UPC	Spain
4	Ontotext AD	Ontotext	Bulgaria
5	<del>Matrixware GmbH.</del>	<del>MXW</del>	<del>Austria</del>

# WP1: General view

## Work package leaders

WP1: Management	UGOT	1	36	Aarne
WP2: Grammar Developer's Tools	UGOT	1	24	Aarne
WP3: Translator's Tools	UHEL	7	30	Lauri
WP4: Knowledge Engineering	Ontotext	1	24	Borislav
WP5: Statistical and Robust Translation	UPC	7	30	Lluís
WP6: Case Study: Mathematics	UPC	7	30	Jordi
WP7: Case Study: Patents	UPC	10	33	Cristina
WP8: Case Study: Cultural Heritage	UGOT	13	30	Aarne
WP9: User Requirements and Evaluation	UHEL	1	36	Lauri
WP10: Dissemination and Exploitation	UGOT	1	36	Olga

# WP1: General view

## Management structure

- Coordinator
  - Project Manager
- Site leaders

### Steering Group

- convene at project meetings
- resolve conflicts
- decide any major change



# WP1: General view

## Advisory Board

- perform independent quality assurance
- external experts
- attend the annual meetings
- deliver assessment reports to us and the EC

**Keith Hall** (Google Zurich) –  
Researcher

**Stephen Pulman** (Oxford) - Professor  
of Computational Linguistics

# WP1: General view

## Deliverables

Number	Title	Due date
D1.1	Work Plan for MOLTO	M1
D1.2,4,6	Periodic management report 1,3,5	M7, M19, M31
D1.3,5	Periodic management report 2,4	M13, M25
D1.7	Final management report	M36
DX. 1.1,2,3	Annual Public Report	15 Nov. 2010, 2011, 2012

# WP1: General view

## Project documentation (Annex X)

- Fact sheet (*M1*)
- Web site (*M3*)
- HTML Presentation (*M3*)
- DVD or web showcase (*M37*)



# WP1: Description of work

## Termination of Matrixware

- MXW left Consortium in April 2010
- Negotiations with EPO
- Amendment of Consortium Agreement
- Amendment of budget
- Amendment of Annex I , DoW (12/02/2010)
- Contract amendment signed 1 March 2011, effective 23 April 2010



# WP1: Description of work

## DoW Amendment


MXW's tasks and pm's are distributed to other partners:

- WP7 work distributed to UGOT, Ontotext, UPC
- WP7 leader is UPC, with Cristina España as the WP leader
- WP7 starts month 10 and ends month 33
  - deliverables postponed by 4 months
  - Milestone 9 postponed to M33

All other WP's, deliverables, and milestones retain their schedule from the original DoW.


# WP1: Description of work

## Timeplan revision

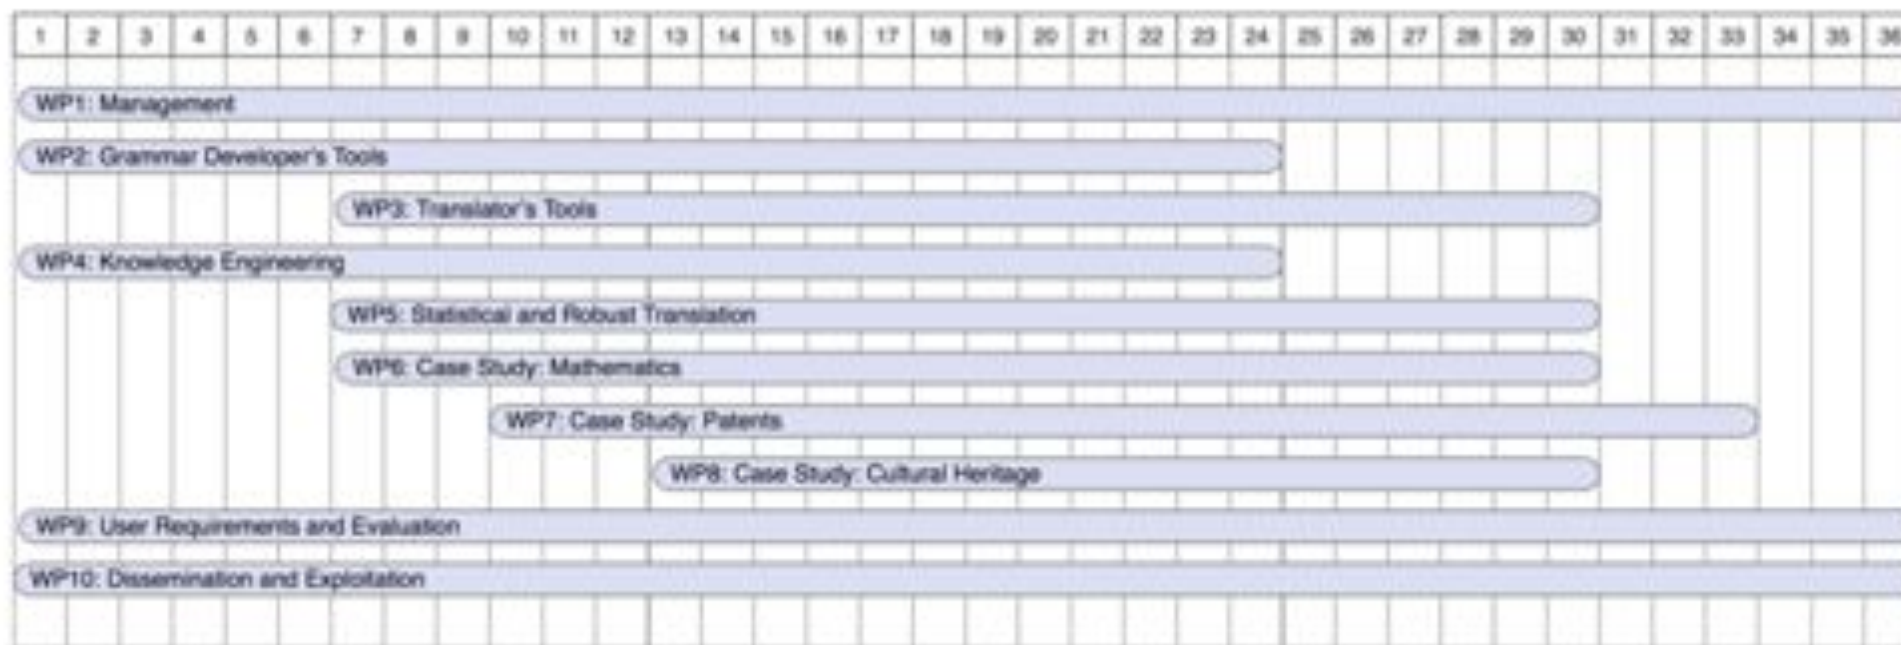

# WP1: Description of work

## Reallocation of PMs

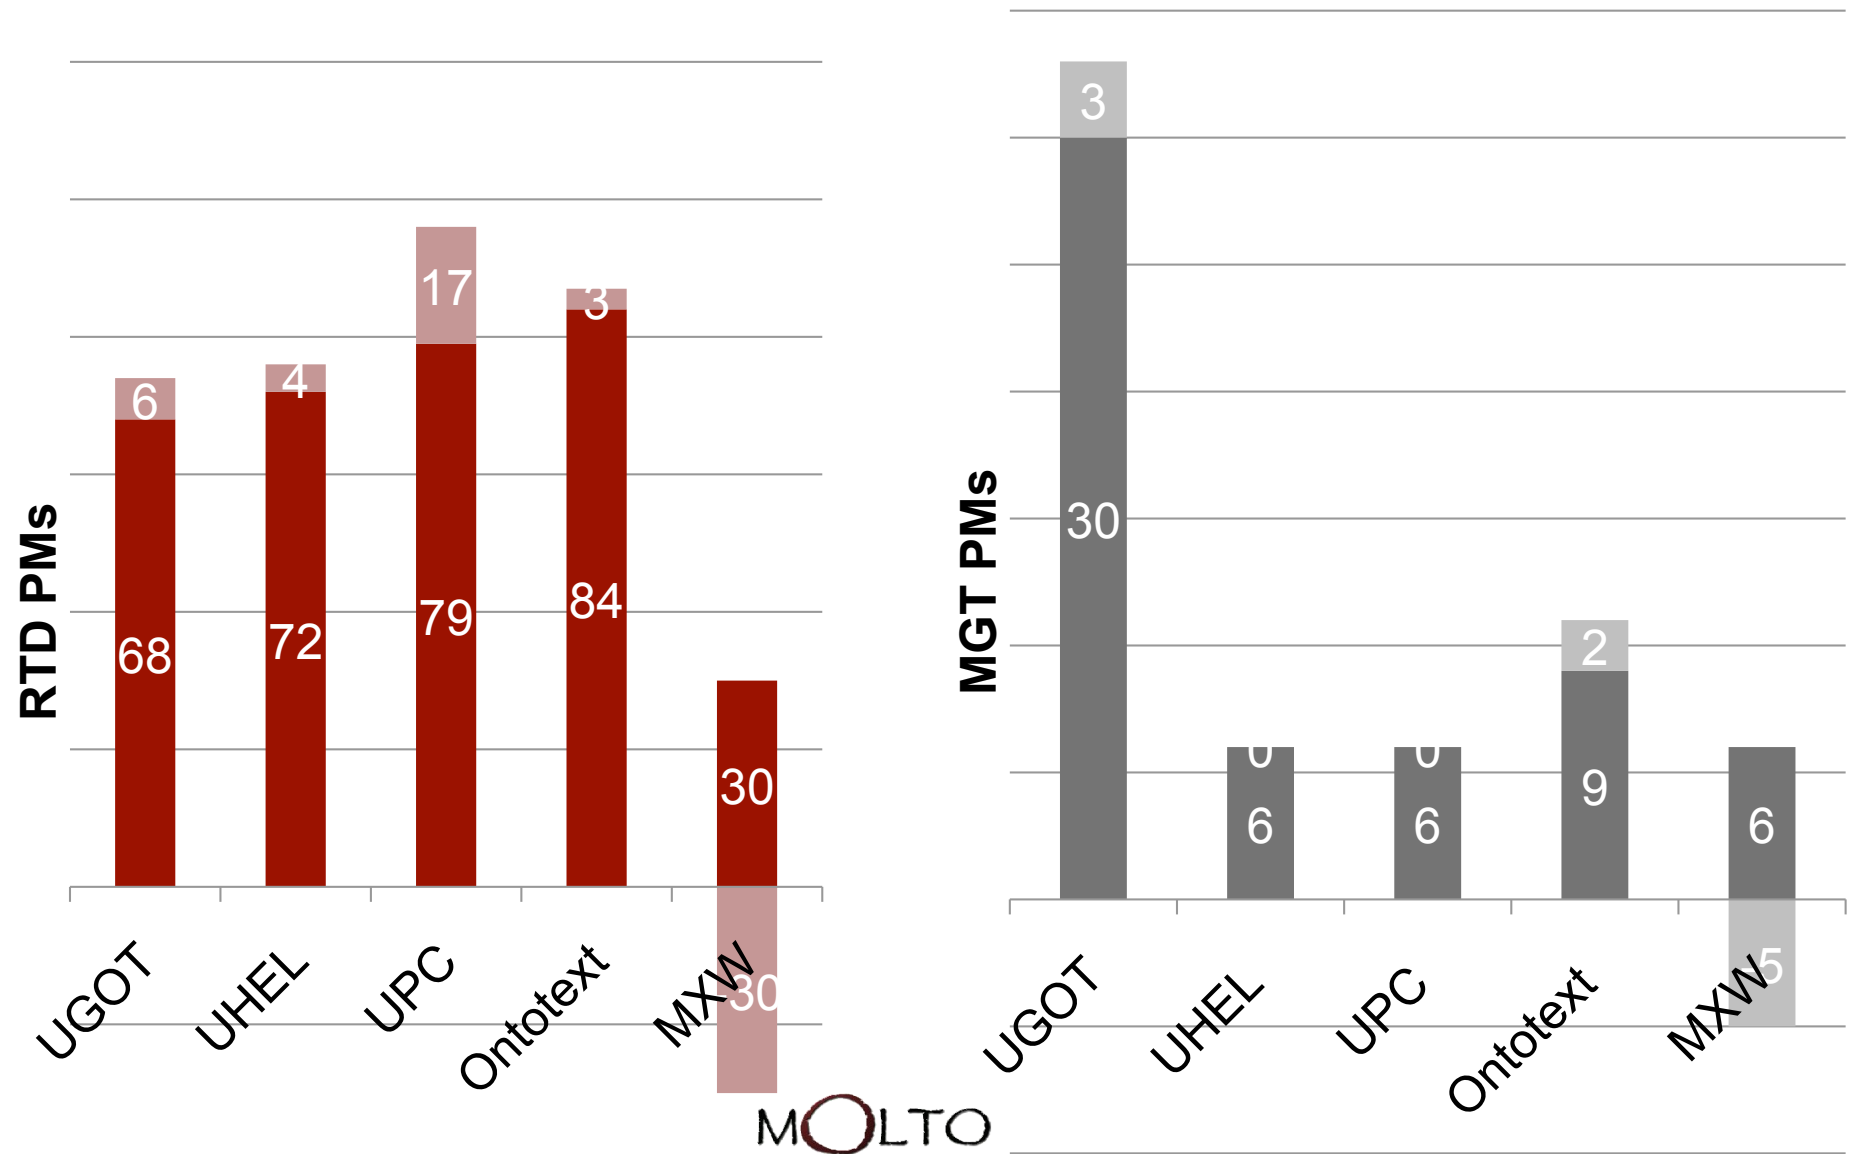

# WP1: Description of work

## Resources reallocation

Partner	RTD pm's	MGT pm's
UGOT	74/68	33/30
UHEL	76/72	6/6
UPC	96/79	6/6
Ontotext	87/84	11/9
MXW	0/30	1/6
Total	333/333	57/57

# WP1: Description of work

## Gender aspects



Luxemburg, 15 March 2011

MOLTO

# WP1: Management

## MOLTO - Enlarged EU (FP7-ICT-2011-7)

Small or medium-scale focused research project (STREP) ICT Call 7

Date of preparation: 18.01.2011

Work programme topic addressed: ICT 2011.11.3

- Leader: UGOT
- Participants: U Zurich, Be Informed, UHEL
- Start: M1, 1 Aug 2011
- End: M18, 28 February 2013
- Person months: 73PMs, (10 MGT, 63 RTD)
- Objectives:
  - Multilingual wiki system (wiki scenario)
  - Localization of interactive knowledge-based systems

# WP1: Future work

## Deliverables

Number	Title	Due date
D1.1	Work Plan for MOLTO	M1
D1.2,4,6	Periodic management report 1,3,5	M7, M19, M31
D1.3,5	Periodic management report 2,4	M13, M25
D1.7	Final management report	M36
DX. 1.1,2,3	Annual Public Report	15 Nov. 2010, 2011, 2012



# ADDITIONAL SLIDES

# WP1: Management

## EPO Negotiations

- Fri, Feb 5, 2010, EPO contacted us to be in touch wrt effort to provide multilingual patents
- 19/05/10, EU tells us to stop negotiations with IRF
- 20/05/10 invitation to EPO to be partner
- 21/05/10, EPO sends us reply with ok to provide the data and help in evaluation and exploitation, for partnership we have to wait
- 25/05/10, EPO says that decision to distribute their aligned corpora for MT purposes should be finalized in October.
- 10/11/2010, we request an answer to EPO concerning membership
- 10/11/2010, EPO declines being partner but promises the corpora
- redistribution of work, amendment of DoW
- 21/12/2010, e-mail to EPO concerning release of corpora
- 3/2/2011, letter to EPO president to request release of corpora


# WP1: Description of work

## Timeplan



# WP1: Description of work

## MOLTO budget – Requested EC contribution for RTD

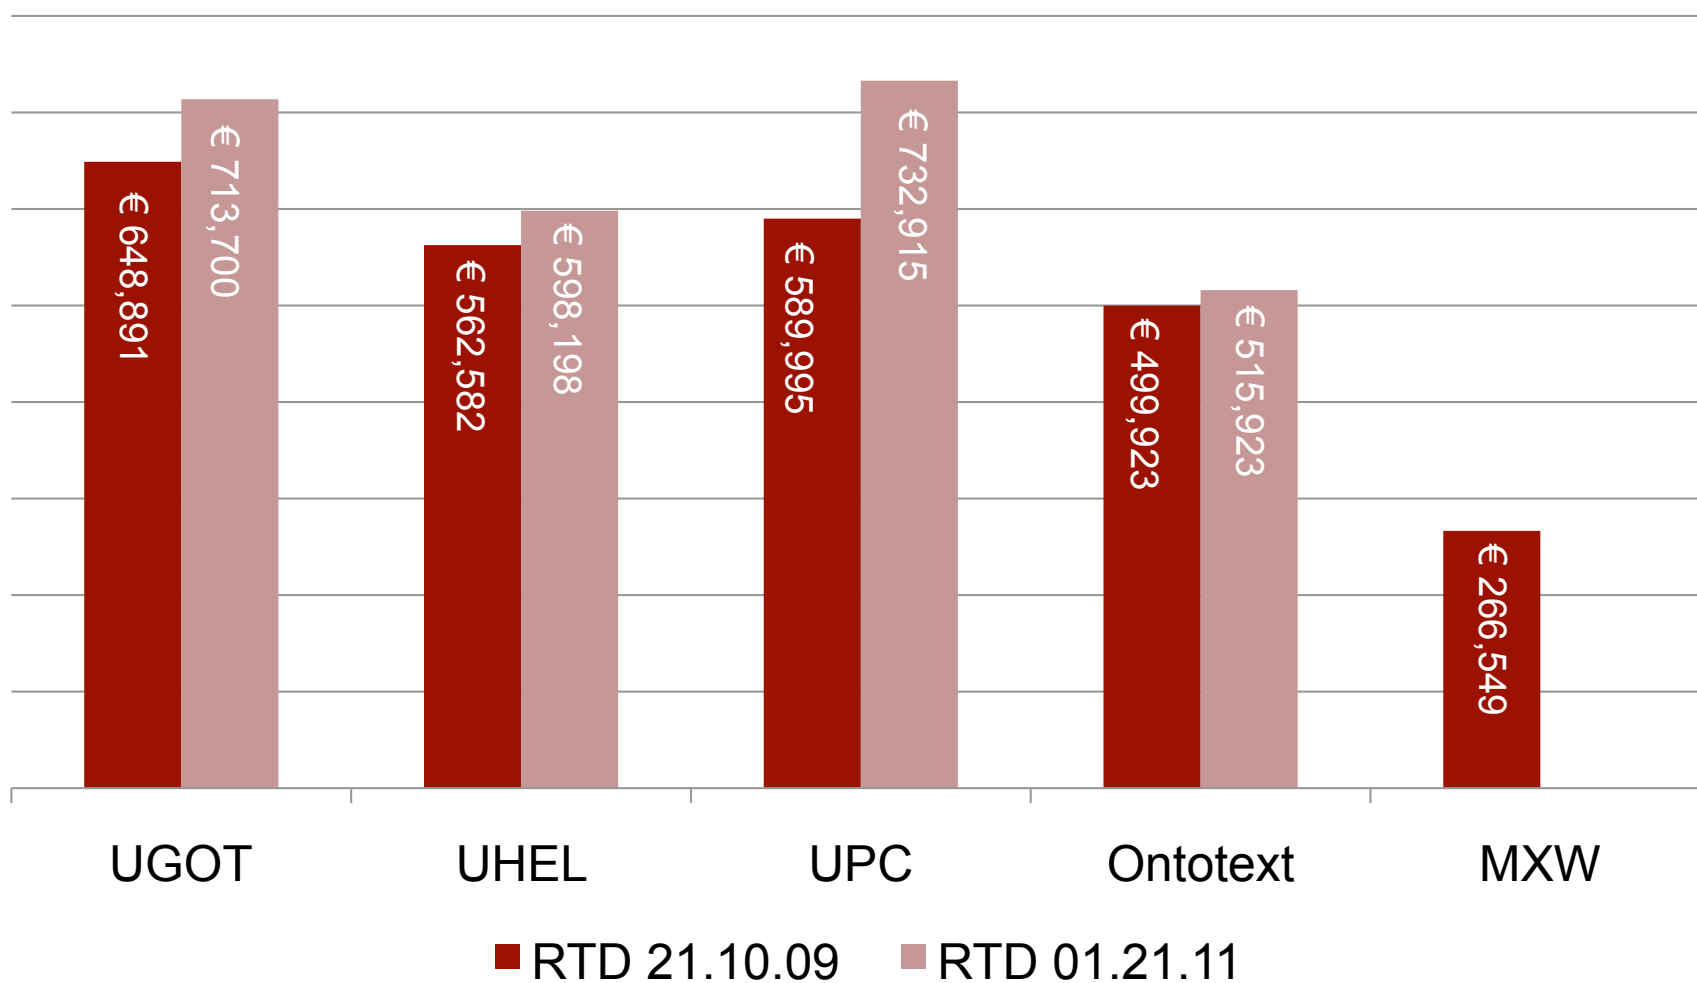

# WP1: Description of work

## MOLTO budget – Requested EC contribution for MGT

